
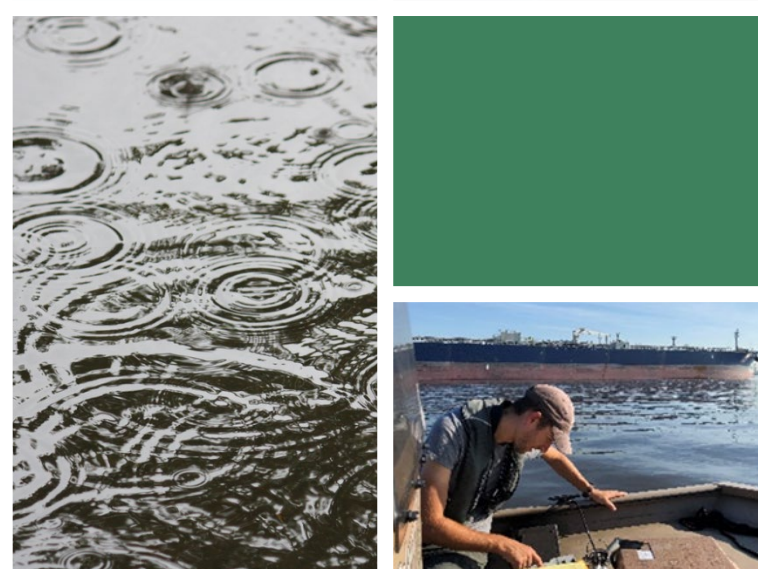


Presented to an advisory committee of the DRBC on June 3, 2026. Contents should not be published or re-posted in whole or in part without the permission of DRBC.

Storage Study Phase II Update

Chad Pindar, P.E.
Manager of Water Resource Planning

Water Management Advisory
Committee
June 3, 2026



Storage Study Phase II Update – WMAC; June 3, 2026

- Resolution for the Minutes approved in September 2024.
- Two track study with Mott MacDonald (MM)
 - 3 Quarries (Penn Park, Evansville, Moores Station / Trap Rock)
 - Cannonsville expansion
- Requires 3 different contracts
 - DRBC & MM for 3 Quarries – **finalized 3/20/2025** (18 months; Sept 2026)
 - DRBC & NYCDEP for Cannonsville work – **contract agreed to ~ 2/5/2026; internal NYCDEP law review**
 - DRBC & MM for Cannonsville– **pending DRBC/NYCDEP contract**

Storage Study Phase II Update – WMAC; June 3, 2026

- Draft report for the quarries received in mid May 2026 (ahead of schedule)

Next steps

- DRBC review of draft report – comments to MM end of June 2026
- Publish September 2026
- Cannonsville
 - Complete contract between DRBC & NYCDEP
 - Complete DRBC & MM contract
 - Kickoff meeting
